higher education & training

Department:
Higher Education and Training
REPUBLIC OF SOUTH AFRICA

MARKING GUIDELINE

NATIONAL CERTIFICATE (VOCATIONAL)

PROJECT MANAGEMENT
NQF LEVEL 4

22 NOVEMBER 2019

This marking guideline consists of 8 pages.

Copyright reserved

SECTION A

QUESTION 1

1.1	1.1.1	D		
	1.1.2	D		
	1.1.3	A		
	1.1.4	C		
	1.1.5	B	(5 × 1)	(5)
1.2	1.2.1	Trigger event		
	1.2.2	Event		
	1.2.3	Brainstorming		
	1.2.4	Project plan		
	1.2.5	Predecessor	(5 × 1)	(5)
1.3	1.3.1	B		
	1.3.2	F		
	1.3.3	A		
	1.3.4	C		
	1.3.5	D	(5 × 1)	(5)
1.4	1.4.1	False		
	1.4.2	True		
	1.4.3	False		
	1.4.4	True		
	1.4.5	True	(5 × 1)	(5)
				[20]

TOTAL SECTION A: 20

SECTION B

QUESTION 2

2.1 2.1.1 Community project

2.1.2 Empower children and youth of previously disadvantaged communities to become independent. (2 × 2) (4)

2.2 2.2.1 A project plan is a formal, approved document used to manage and control the project execution. (2)

2.2.2
- The life span of the project
- The projected cost
- Tasks and activities
- Resources needed
- Objectives of the project
- Time frame
- People involved in executing the tasks
- Procedures and solutions in case of problems and unexpected changes (Any 4 × 1) (4)

2.2.3 One shot project delivery strategy (2)

2.3 2.3.1
- Perseverance
- Clear communication
- Non-judgemental conduct
- Ability to resolve conflict
- Positive attitude
- Conceptual skills
- Leadership skills.
- Management skills
- Interpersonal skills
- Negotiation skills (Any 4 × 1) (4)

2.3.2
- Project processes and procedures should be explained to the team.
- Project tasks should be adequately defined to prevent confusion amongst team members.
- Project objectives should be clearly communicated.
- Reporting processes should be communicated.
- Team members should know exactly what is expected from them.
- Team members must be made aware of budgetary constraints.

(Any 4 × 2) (8)

Copyright reserved

2.3.3 The MaciusRestis Charitable Trust (2)

2.3.4
- They are responsible for funding the project.
- Authorise payment (2)

2.3.5
- Kayamandi Community volunteers- unemployed parents
- Project Manager – Asanda Ngeni
- Team Leaders – Mama Aloni and Mama Fibi
- Community leaders
- Children and the elderly (Any 4 × 1) (4)

[32]

QUESTION 3

3.1 3.1.1
- Explain team members' responsibilities with them so that they understand their responsibilities.
- Involve team members in developing the outcomes of their activities.
- Team members should know what to do.
- Discuss team members' performances with them.
- Use people's strengths and turn weaknesses into strengths.
- Train and manage team members.
- Ensure that the necessary resources are available.
- Respond to change requests by adapting processes and procedures as needed.
- Manage communication channels with team members, between teams, and with management. (Any 6 × 1) (6)

3.1.2
- Define the tasks, activities and responsibilities the team leader will be delegating.
- Select a competent delegate to carry the authority and shoulder the responsibility.
- Specify the organisational and informational relationships and the limits of authority.
- Establish controls to ensure that the authority is properly used.


(4 × 2) (8)

3.2 Finish-to-start dependency
- The 'from' activity must finish before the 'to' activity can start.
- The ingredients for food must be acquired first before they can be prepared.

Start-to-finish dependency
- The 'from' activity must start before the 'to' activity can finish.
- The food must first be prepared before the children can be fed.

(2 × 2) (4)

3.3

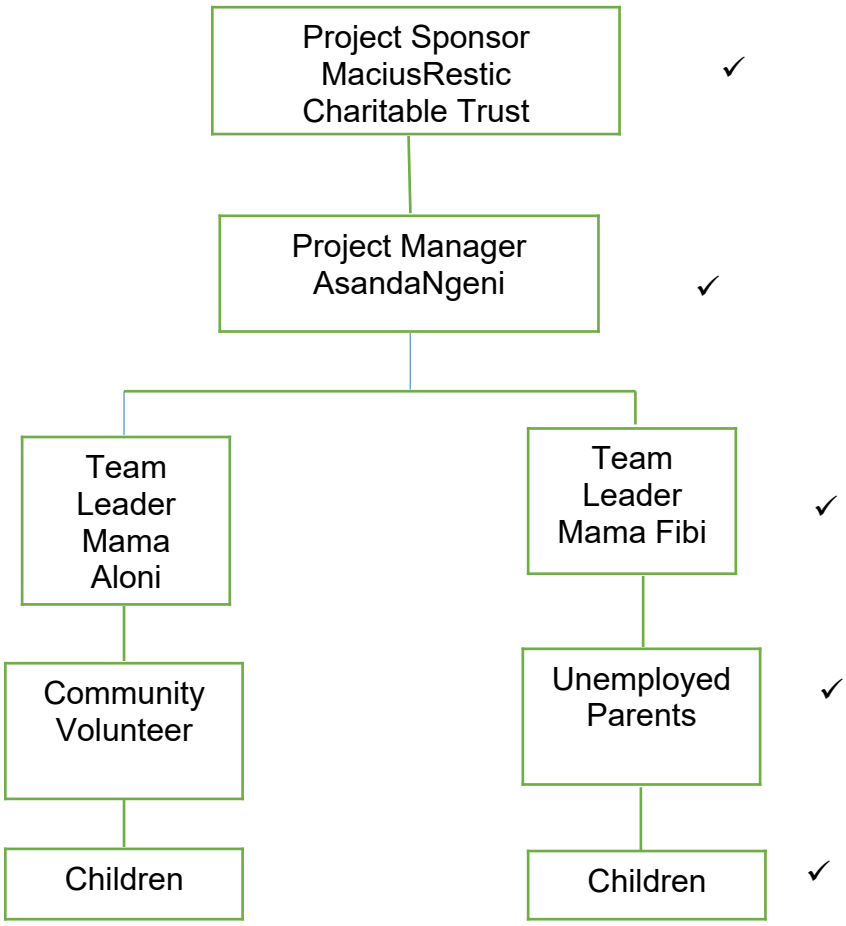

(5 × 1) (5)

3.4 3.4.1

- The work that needs to be done (tasks).
- Who needs to do it (team members)?
- When the work will start?
- When the work will be finished?
- What are the dependencies that exist between the tasks?
- Who will supply the resources?
- What will it cost to finish the work on time? (Any 4 × 1) (4)

3.4.2

- Identify the major project deliverables for the entire project and for each phase of the project.
- Identify major milestones at the end of each phase of the project.
- Put project teams together.
- Identify risks and their possible impact.
- Control the budget. (Any 4 × 2) (8)

[35]

QUESTION 4

4.1 4.1.1
- Physical resources
- Financial resources
- Human resources
- Achieve project objectives
- Time management
- Quality control
- Information management (Any 4 × 1) (4)

4.1.2
- Not sufficient supplies to feed all the children.
- Equipment breaking down.
- Communication breakdown.
- Resources (ingredients) unavailable.
- Late delivery of supplies.
- Environmental hazards (Infected supplies - listeriosis).

(Any 3 × 1) (3)

4.1.3
- Children will go hungry.
- If equipment breaks down, no food can be prepared.
- Cannot prepare and deliver food to the children on time.
- Children can get sick. (Any 2 × 1) (2)

4.1.4
STEP 1: Identify the problem.
STEP 2: Suggest possible solutions/Analyse the problem.
STEP 3: Assess the solutions/Generate potential solution.
STEP 4: Choose the best solution/Select and plan the solution.
STEP 5: Implement the solution.
STEP 6: Review implementation of the solution/Evaluate the solution. (6 × 1) (6)

4.1.5
- Check if the ingredients for preparing food have not expired.
- Check if the area where food is prepared is clean and not contaminated. (2 × 2) (4)

4.2 4.2.1
- Telephone
- Fax
- Email
- Status reports
- Project newsletter
- SMS (short message service)
- Meetings
- Face to face
- Video conferencing (Any 4 × 1) (4)

4.2.2
- To monitor and evaluate progress as measured against the project plan and to determine the project status.

Copyright reserved

- To make adjustments necessary to correct deviations from the project plan.
- To identify and resolve issues that may hinder the successful completion of the project.
- Performance highlights and updates on work completed.
- Problems and issues.
- Approved changes to the project plan.
- Risk management status updates.
- Lessons learnt in executing and controlling processes.

(Any 3 × 1) (3)

4.2.3
- Request title.
- Originator's name.
- Originator's contact details such as email, phone number.
- Description of the proposed change.
- Reasons for the change and possible benefit of the change.
- The urgency of the request – originator will assign a priority to the change request. (Any 3 × 1) (3)

[29]

QUESTION 5

5.1 5.1.1 Risk is defined as an uncertain event or condition that should it occur, will have a positive or negative effect on the project's objectives. (2)

5.1.2
- Use the correct protective clothing and equipment as required by the job.
- Implement and comply with the relevant procedures, material requirements and methodologies in maintaining prescribed health, safety and environmental standards in the workplace.
- Implement selected mechanism for safety, health and environmental impacts and risks. (3 × 2) (6)

5.1.3
- Observations – randomly by watching project activities as they take place.
- Regular reviews – meet to discuss progress.
- Scheduled evaluations – compare the actual quality performance against the planned performance. (3 × 2) (6)

5.2 It is a process to ensure that all project activities necessary to design, plan and implement a project are effective and efficient with respect to the purpose of the objective and its performance.

OR

It is a number of quality reviews that are completed to ensure that the project produces deliverables to the required standard. (2)

5.3
- The deliverable will not be of the quality described in the project.
- It could lead to accidents and loss of life.
- The project manager will not be able to obtain sign off from the customer or stakeholders.
- The money due for the project will not be paid.
- The project teams and suppliers will not be paid.
- The project will be a failure. (Any 3 × 2) (6)

5.4
- Evaluation should be impartial, and should be done by people involved in the project.
- The evaluator should have experience and expertise.
- The evaluation process should be transparent.
- Presentation of evaluation reports must be clear and concise.
- Evaluation should allow for decision-making improvement and future planning. (Any 3 × 2) (6)

5.5
- Engage key stakeholders in a democratic, participative style.
- Identify the right people for the right role.
- Delegate key components of the project, as needed.
- Consult others when necessary in decision-making.
- Develop effective leadership skills and employ them as needed during the project cycle. (Any 2 × 1) (2)

5.6
- To avoid making the same mistakes in future projects.
- To have contingency plans that worked.
- For review purposes.
- Cost-saving technique.
- To reduce the risks.
- To save time. (Any 4 × 1) (4)

[34]

TOTAL SECTION B: 120
GRAND TOTAL: 150
